

Sprint 2 Burndown Chart Analysis

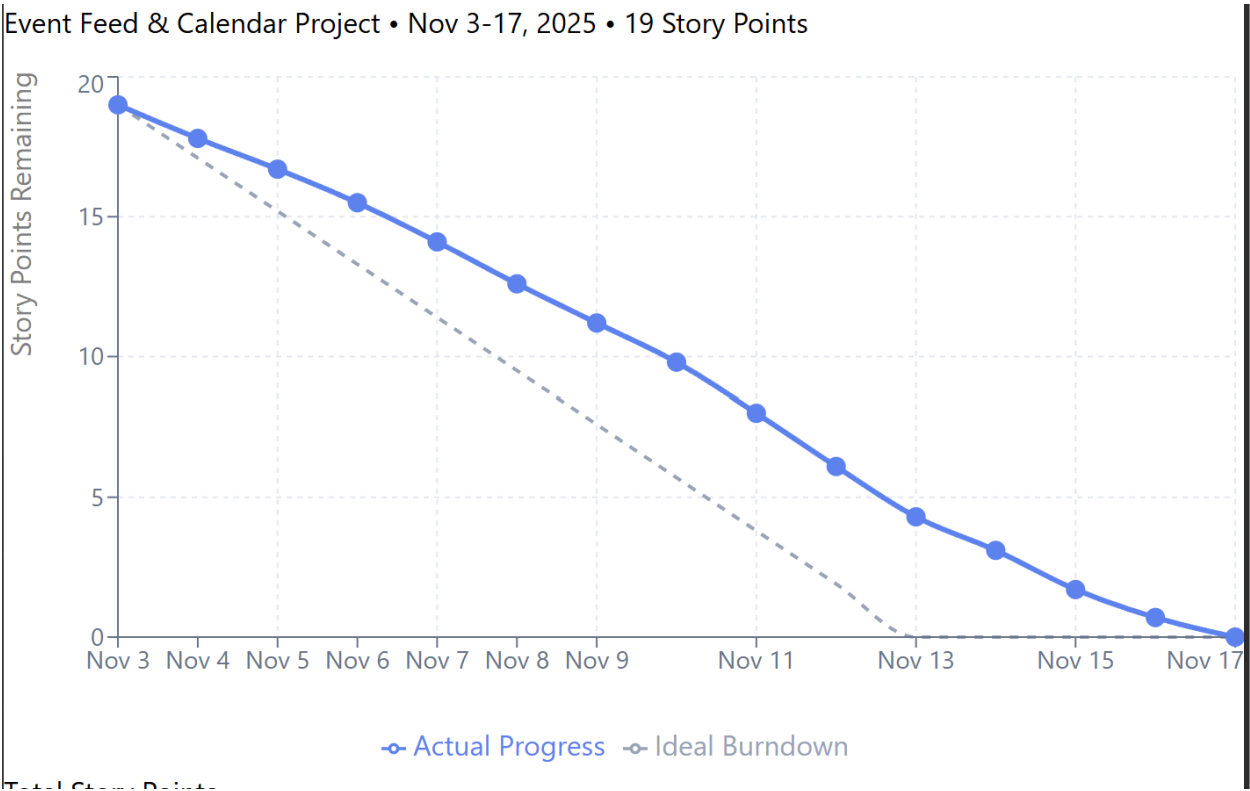


Figure 1: Sprint 2 Burndown Chart: Event Feed & Calendar Project (Nov 3-17, 2025)

Sprint Overview

Sprint 2 Metrics	
Total Story Points:	19 points
Planned Duration:	10 days (Nov 3-13)
Actual Duration:	14 days (Nov 3-17)
Planned Velocity:	1.9 points/day
Actual Velocity:	1.36 points/day
Sprint Extension:	+4 days

Burndown Chart Analysis

The burndown chart shows our team maintained consistent progress throughout the sprint, burning down story points at a steady rate of approximately 1.36 points per day. However, we required a 4-day extension beyond our original November 13th deadline to complete all committed work.

Key observations:

- **Steady Progress:** The team showed consistent daily effort without major blockers
- **Scope Delivered:** All 19 story points were successfully completed
- **Schedule Variance:** Original 10-day estimate proved insufficient for the workload

- **Final Push:** The team maintained momentum through the extension period

Velocity Comparison with Sprint 1

Velocity Comparison

Metric	Sprint 1	Sprint 2
Total Points	18 points	19 points
Duration	14 days	14 days
Velocity	1.29 points/day	1.36 points/day
Scope Delivered	83% (15/18 pts)	100% (19/19 pts)

Velocity Change Analysis

Our velocity **increased by 5%** from Sprint 1 to Sprint 2, from 1.29 to 1.36 points per day. This modest improvement occurred despite both sprints running for the same 2-week duration.

Why velocity increased slightly:

1. Team Experience & Process Improvement

- Better understanding of the codebase and development workflow
- Improved estimation accuracy from Sprint 1 learnings
- More effective task breakdown and assignment

2. Scope Management

- Sprint 1: One feature (3 points) didn't make it to production
- Sprint 2: All committed features delivered to production
- Better definition of "done" and acceptance criteria

3. Technical Foundation

- Reduced setup and configuration time
- Established development patterns and code standards
- Reusable components from previous sprint

Key Insights

Primary Finding

While our velocity improved by 5% and we delivered 100% of scope (compared to 83% in Sprint 1), we still underestimated the total effort required. The team demonstrated consistent productivity but our initial planning was too optimistic about completing 19 points in 10 days.

Recommendations for Sprint 3

1. **Realistic Planning:** Plan for 14-day sprints consistently rather than 10-day targets
2. **Maintain Consistent Velocity:** Target 1.3-1.4 points/day based on demonstrated capacity
3. **Scope Commitment:** Continue 100% scope delivery by committing to achievable targets
4. **Early Critical Path:** Start critical path work immediately in the sprint

Conclusion

Sprint 2 demonstrated steady team performance with a 5% velocity increase and 100% scope delivery. The burndown chart confirms consistent team performance at approximately 1.36 points per day. For Sprint 3, we will maintain our reliable delivery rate while adopting more realistic timeline expectations based on our demonstrated capacity.
